

Project News

Driving forward the Woking Integrated Transport Project

May 2017

Since our previous newsletter at the beginning of April we have seen two areas of the project take shape, The Broadway and the new High Street link road. The Broadway works are complete on the south side with all the new paving stones fitted – see photo on next page. The new paving demonstrates the visual appeal and space enhancement that can be expected when the project is completed, benefitting both businesses and pedestrians.

Thank you for your feedback


The consultation on the series of new Permanent Traffic Regulation Orders, detailed on page 2 in the April issue, closed on the 27 April 2017. We are currently reviewing your feedback that was submitted by you.

High Street link road

The opening for the new link road, between High Street and Victoria Way by Victoria Arch, has unfortunately been pushed back by a month. This is due to the complex utility diversions within the old market square. It is now anticipated the new link road will open in mid June.

High Street vehicle restrictions

The delay in completion of the new link road means that vehicular access restrictions for High Street, that will introduce a one-way westbound route for buses, cycle path and authorised vehicles only between 7am and 9pm, will also be delayed.

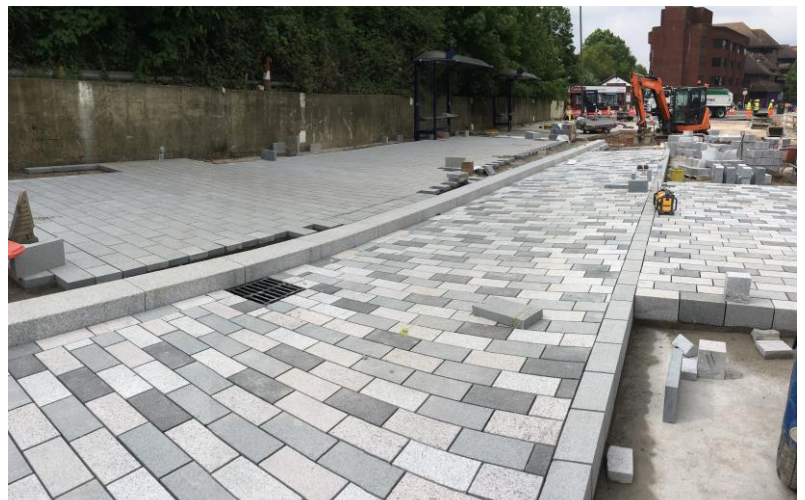

New paving going in on the new link road.

The proposals to install an automated number plate recognition (ANPR) system, for the enforcement of vehicle restrictions on High Street, has also been delayed for the reasons mentioned above.

We will contact local residents and businesses directly affected by these restrictions separately to explain more about the criteria and the process of authorising vehicles.

Chertsey Road

The works to Chertsey Road are on schedule and you will start to see the installation of a new kerb line in the early part of this month and the installation of new surfacing down towards the roundabout end from mid May.

Cawsey Way

Cawsey Way will remain open in the current westbound direction only until the new link road has opened.

Albion Square Canopy

Discussions to plan the removal of the canopy have taken place with developer and Network Rail. We will inform you of the proposed dates as soon as they have been agreed.

The Broadway

The south side of The Broadway is now completed and works have moved to the north side of the road to pave the footway outside the shops and businesses.

As can be seen from the photo, the space between the newly paved road and the temporary fencing does not allow for the bus stops to be put back into safe operation until the north side works are complete.

The planned completion date for The Broadway has been moved back to the end of July. The reason for this extension is due to the need for forward planning underground utilities that will prevent the need to dig up the new road surface in the future.



The south side of The Broadway looking east.

For the latest updates on all the roads in the Woking Integrated Transport Package, please regularly visit www.woking.gov.uk/wokingitp

Who to contact if you have a query?

If you have queries regarding the construction process, please contact Farrans Construction, on **02890 394043**.

Alternatively, if you have any queries regarding the project, please email the project team at wokingitp@woking.gov.uk
